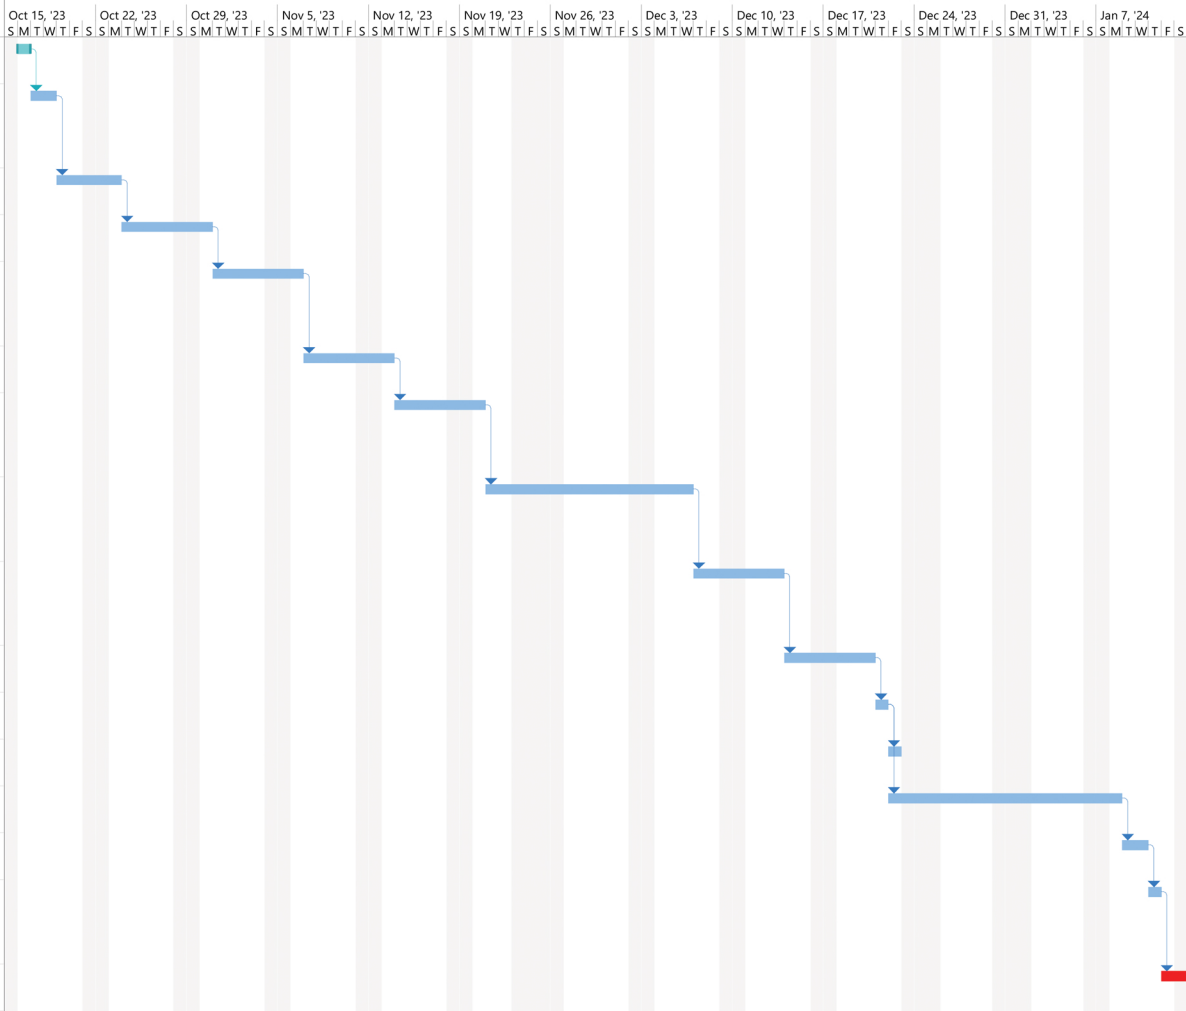ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1			Mobilization	1 day	Mon 10/16/2	Mon 10/16/2		
2			Set Up Barricades & Temporary Facilities	2 days	Tue 10/17/23	Wed 10/18/23	1	
3			Demo Asphalt	3 days	Thu 10/19/2	Mon 10/23/2	2	
4			Pile Driving	5 days	Tue 10/24/2	Mon 10/30/2	3	
5			Foundation Excavation	5 days	Tue 10/31/23	Mon 11/6/23	4	
6			MEP Excavation	5 days	Tue 11/7/23	Mon 11/13/2	5	
7			Install Underslab Utilities	5 days	Tue 11/14/23	Mon 11/20/23	6	
8			Foundation Backfill / Slab Prep	10 days	Tue 11/21/23	Wed 12/6/23	7	
9			Place Concrete Forms	5 days	Thu 12/7/23	Wed 12/13/23	8	
10			Place & Tie Rebar	5 days	Thu 12/14/2	Wed 12/20/2	9	
11			Pour Slab	1 day	Thu 12/21/2	Thu 12/21/2	10	
12			Cut Control Joints	1 day	Fri 12/22/23	Fri 12/22/23	11	
13			Slab Curing	10 days	Fri 12/22/23	Mon 1/8/24	11	
14			Strip Forms & Cleanu	2 days	Tue 1/9/24	Wed 1/10/24	13	
15			Mobe Out for Season	1 day	Thu 1/11/24	Thu 1/11/24	14	
16			Seasonal Shutdown	70 days	Fri 1/12/24	Fri 4/19/24	15
